



# Arlington High School Building Project

AHS Construction Update – April 4<sup>th</sup>, 2024

## Arlington HS Construction Schedule: April 2020 – September 2025

### Construction Details

Phase 1 and 2 construction is complete and all parts of the new school are finished except for the athletics wing. The new Menotomy Preschool and new district offices are also complete. Phase 3 has begun where part of the old school will be demolished. Those areas are closed off from the existing school during the next phase of construction.

### COVID-19 Update


The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates  
<https://ahsbuilding.org/news/construction-updates/>  
For more information, visit:  
[www.ahsbuilding.org](http://www.ahsbuilding.org)  
Email questions or concerns to:  
[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative,  
(617) 352-8593



### PHASE 3 BUILDING CONSTRUCTION (November 2023 – February 2025)

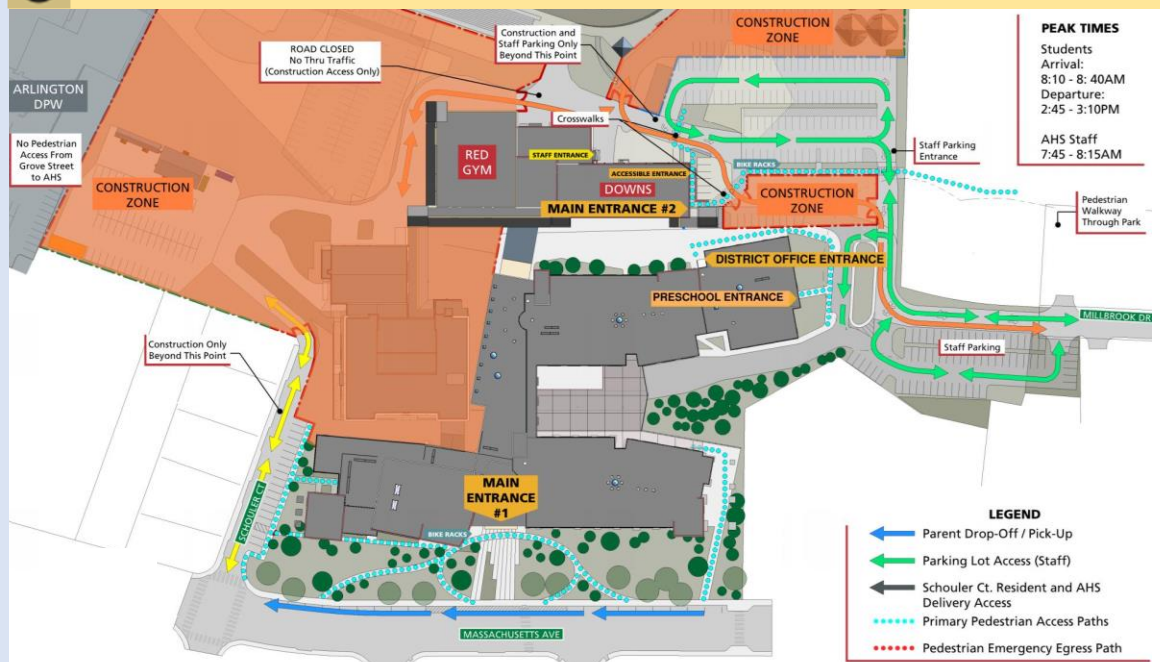

### Construction Look Ahead – Week of April 8<sup>th</sup>, 2024

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts:

- Deliveries ongoing

#### General Site Activities:

- Continue formwork of footings in preparation for concrete pour.
- Continue coordinating concrete pour of footings.
- Sitework for Minuteman Bike Path
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Start underground plumbing and electrical
- Schouler Court:
  - Closed to public Access, except abutters as of 11/8/23. Construction vehicles entering and exiting project site.

#### Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.



**ARLINGTON HIGH SCHOOL**  
**WEEKLY UPDATE – WEEK OF APRIL 8<sup>TH</sup> 2024**



***Photograph 1: Layout grade beams and tie-in locations.***



***Photograph 2 Layout grade beams & pile caps.***



## ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF APRIL 8<sup>TH</sup> 2024



*Photograph 3: Phase 3 West Elevation (Scholuer Ct)*
